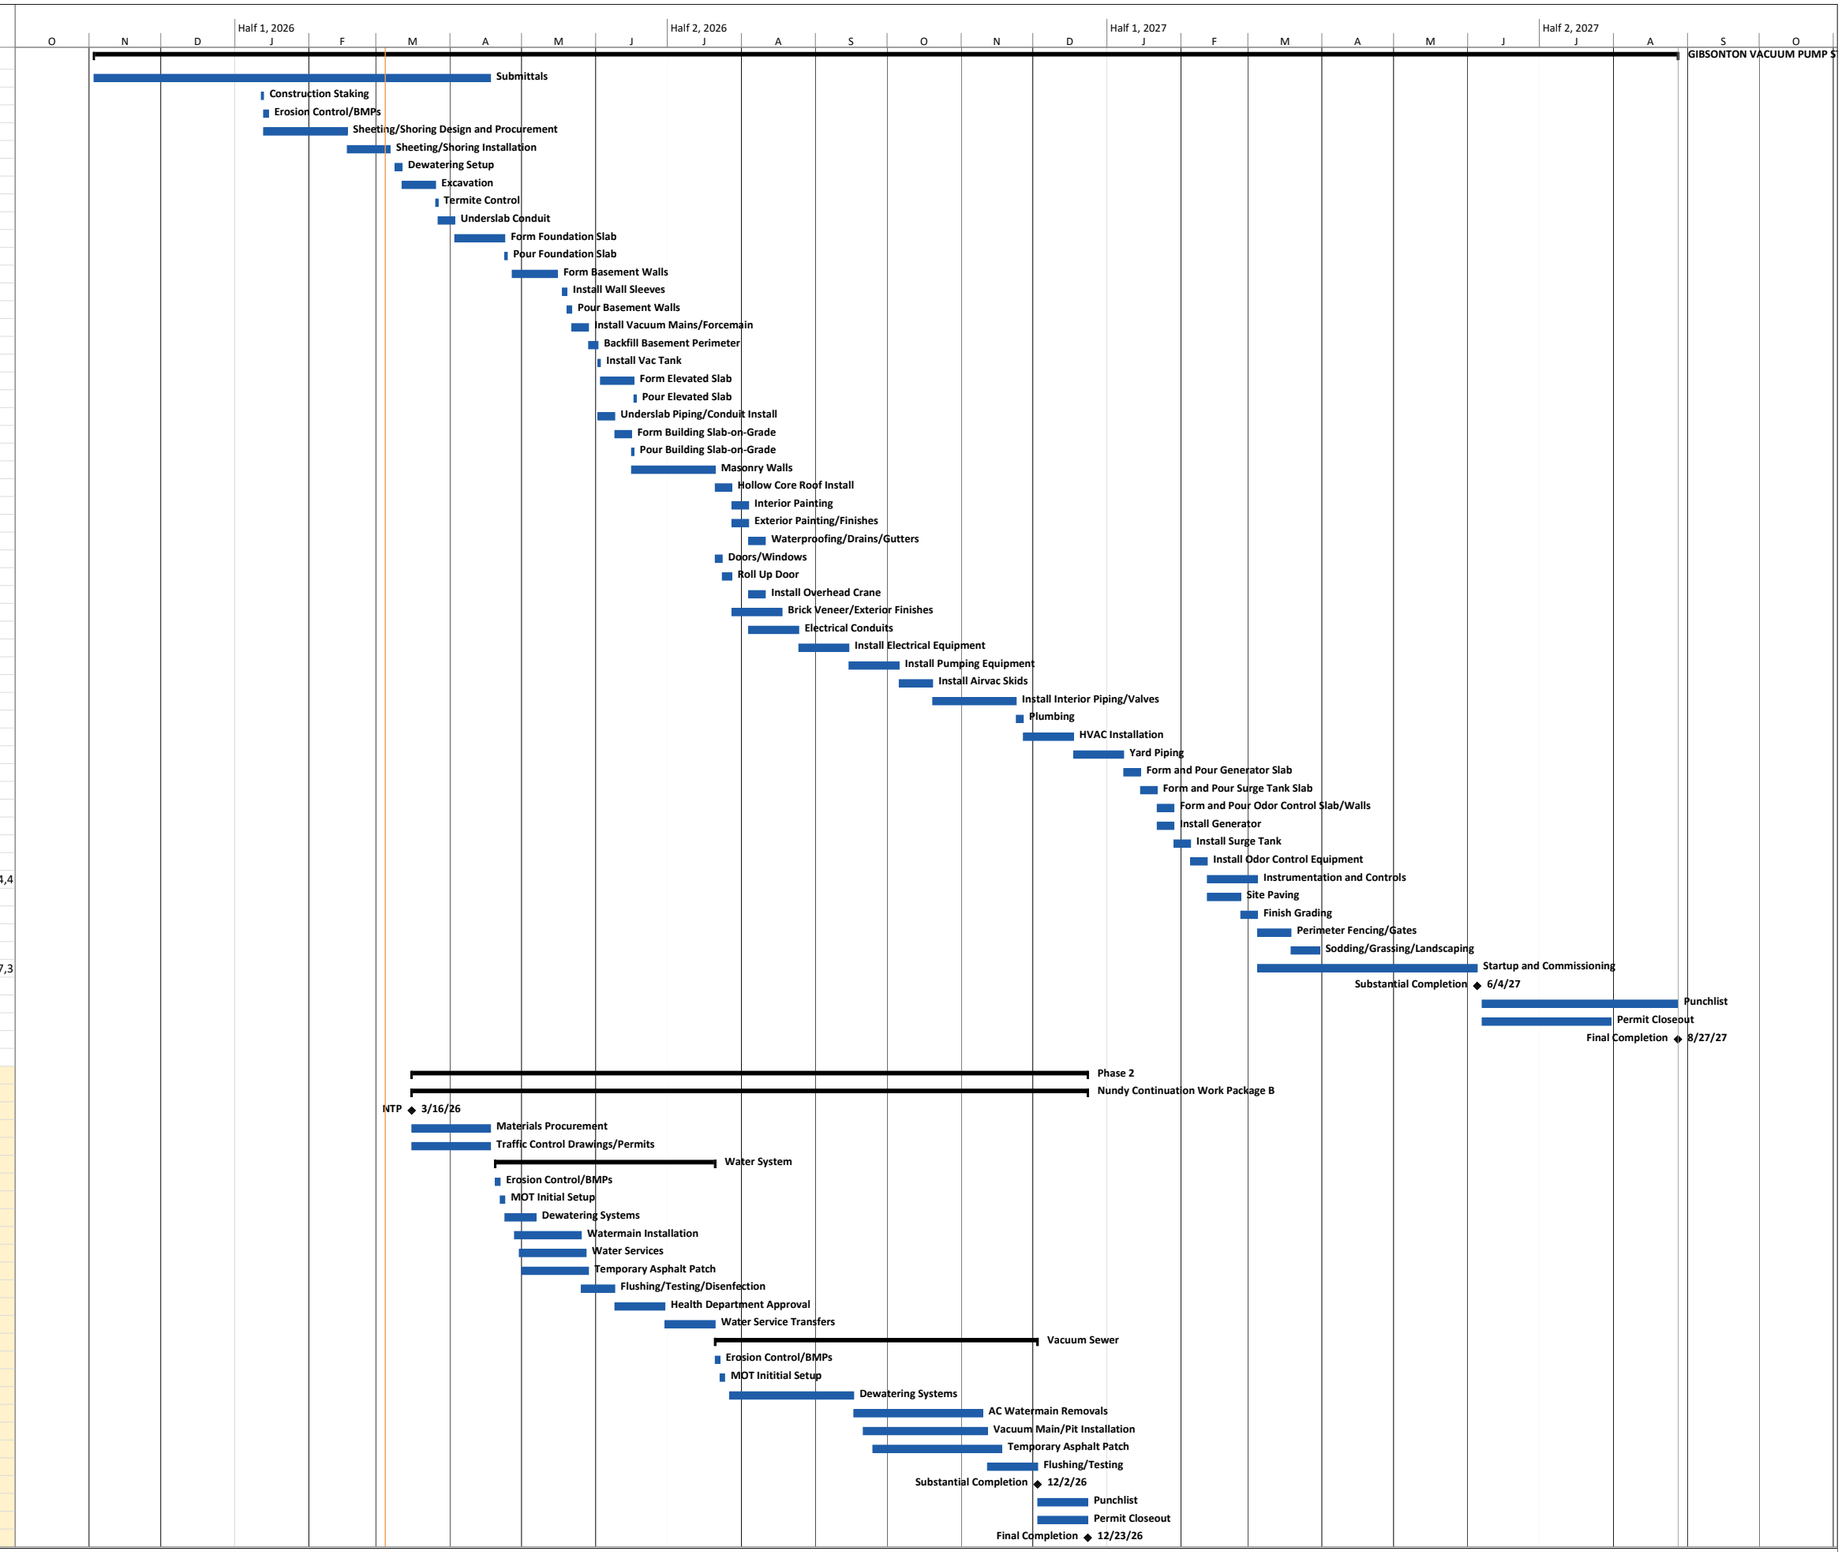ID	% Comple	Task Name	Start	Finish	Duration	Predecessors
1	**0%**	**GIBSONTON VACUUM PUMP STAT**	**Mon 11/3/2**	**Fri 8/27/27**	**475 days**	
2	0%	Submittals	Mon 11/3/25	Fri 4/17/26	120 days	
3	0%	Construction Staking	Mon 1/12/26	Mon 1/12/26	1 day	
4	0%	Erosion Control/BMPs	Tue 1/13/26	Wed 1/14/26	2 days	3
5	0%	Sheeting/Shoring Design and Procurement	Tue 1/13/26	Mon 2/16/26	25 days	3
6	0%	Sheeting/Shoring Installation	Tue 2/17/26	Fri 3/6/26	14 days	5
7	0%	Dewatering Setup	Mon 3/9/26	Wed 3/11/26	3 days	6
8	0%	Excavation	Thu 3/12/26	Wed 3/25/26	10 days	7,6
9	0%	Termite Control	Thu 3/26/26	Thu 3/26/26	1 day	8
10	0%	Underslab Conduit	Fri 3/27/26	Thu 4/2/26	5 days	9
11	0%	Form Foundation Slab	Fri 4/3/26	Thu 4/23/26	15 days	10
12	0%	Pour Foundation Slab	Fri 4/24/26	Fri 4/24/26	1 day	11
13	0%	Form Basement Walls	Mon 4/27/26	Fri 5/15/26	15 days	12
14	0%	Install Wall Sleeves	Mon 5/18/26	Tue 5/19/26	2 days	13
15	0%	Pour Basement Walls	Wed 5/20/26	Thu 5/21/26	2 days	13,14
16	0%	Install Vacuum Mains/Forcemain	Fri 5/22/26	Thu 5/28/26	5 days	15
17	0%	Backfill Basement Perimeter	Fri 5/29/26	Mon 6/1/26	2 days	16
18	0%	Install Vac Tank	Tue 6/2/26	Tue 6/2/26	1 day	15,17
19	0%	Form Elevated Slab	Wed 6/3/26	Tue 6/16/26	10 days	18,15
20	0%	Pour Elevated Slab	Wed 6/17/26	Wed 6/17/26	1 day	19
21	0%	Underslab Piping/Conduit Install	Tue 6/2/26	Mon 6/8/26	5 days	17
22	0%	Form Building Slab-on-Grade	Tue 6/9/26	Mon 6/15/26	5 days	21
23	0%	Pour Building Slab-on-Grade	Tue 6/16/26	Tue 6/16/26	1 day	22
24	0%	Masonry Walls	Tue 6/16/26	Mon 7/20/26	25 days	22
25	0%	Hollow Core Roof Install	Tue 7/21/26	Mon 7/27/26	5 days	24
26	0%	Interior Painting	Tue 7/28/26	Mon 8/3/26	5 days	25,24
27	0%	Exterior Painting/Finishes	Tue 7/28/26	Mon 8/3/26	5 days	24,25
28	0%	Waterproofing/Drains/Gutters	Tue 8/4/26	Mon 8/10/26	5 days	27,25
29	0%	Doors/Windows	Tue 7/21/26	Thu 7/23/26	3 days	24
30	0%	Roll Up Door	Fri 7/24/26	Mon 7/27/26	2 days	29,24
31	0%	Install Overhead Crane	Tue 8/4/26	Mon 8/10/26	5 days	24,25,26
32	0%	Brick Veneer/Exterior Finishes	Tue 7/28/26	Mon 8/17/26	15 days	24,25
33	0%	Electrical Conduits	Tue 8/4/26	Mon 8/24/26	15 days	24,26
34	0%	Install Electrical Equipment	Tue 8/25/26	Mon 9/14/26	15 days	33
35	0%	Install Pumping Equipment	Tue 9/15/26	Mon 10/5/26	15 days	34
36	0%	Install Airvac Skids	Tue 10/6/26	Mon 10/19/26	10 days	35
37	0%	Install Interior Piping/Valves	Tue 10/20/26	Mon 11/23/26	25 days	34,35,36
38	0%	Plumbing	Tue 11/24/26	Thu 11/26/26	3 days	37
39	0%	HVAC Installation	Fri 11/27/26	Thu 12/17/26	15 days	38
40	0%	Yard Piping	Fri 12/18/26	Thu 1/7/27	15 days	39
41	0%	Form and Pour Generator Slab	Fri 1/8/27	Thu 1/14/27	5 days	40
42	0%	Form and Pour Surge Tank Slab	Fri 1/15/27	Thu 1/21/27	5 days	41
43	0%	Form and Pour Odor Control Slab/Walls	Fri 1/22/27	Thu 1/28/27	5 days	42
44	0%	Install Generator	Fri 1/22/27	Thu 1/28/27	5 days	41FS+5 days
45	0%	Install Surge Tank	Fri 1/29/27	Thu 2/4/27	5 days	42FS+5 days
46	0%	Install Odor Control Equipment	Fri 2/5/27	Thu 2/11/27	5 days	43FS+5 days
47	0%	Instrumentation and Controls	Fri 2/12/27	Thu 3/4/27	15 days	34,35,36,39,44,4
48	0%	Site Paving	Fri 2/12/27	Thu 2/25/27	10 days	44,45,46
49	0%	Finish Grading	Fri 2/26/27	Thu 3/4/27	5 days	48
50	0%	Perimeter Fencing/Gates	Fri 3/5/27	Thu 3/18/27	10 days	49
51	0%	Sodding/Grassing/Landscaping	Fri 3/19/27	Tue 3/30/27	8 days	50
52	0%	Startup and Commissioning	Fri 3/5/27	Fri 6/4/27	66 days	47,34,35,36,37,3
53	0%	Substantial Completion	Fri 6/4/27	Fri 6/4/27	0 days	52
54	0%	Punchlist	Mon 6/7/27	Fri 8/27/27	60 days	53
55	0%	Permit Closeout	Mon 6/7/27	Fri 7/30/27	40 days	53
56	0%	Final Completion	Fri 8/27/27	Fri 8/27/27	0 days	54,55
57						
58	**0%**	**Phase 2**	**Mon 3/16/26**	**Wed 12/23/26**	**203 days**	
59	**0%**	**Nundy Continuation Work Package B**	**Mon 3/16/26**	**Wed 12/23/26**	**203 days**	
60	0%	NTP	Mon 3/16/26	Mon 3/16/26	0 days	
61	0%	Materials Procurement	Mon 3/16/26	Fri 4/17/26	25 days	60
62	0%	Traffic Control Drawings/Permits	Mon 3/16/26	Fri 4/17/26	25 days	60
63	**0%**	**Water System**	**Mon 4/20/26**	**Mon 7/20/26**	**66 days**	
64	0%	Erosion Control/BMPs	Mon 4/20/26	Tue 4/21/26	2 days	61,62
65	0%	MOT Initial Setup	Wed 4/22/26	Thu 4/23/26	2 days	64
66	0%	Dewatering Systems	Fri 4/24/26	Wed 5/6/26	9 days	65
67	0%	Watermain Installation	Tue 4/28/26	Mon 5/25/26	20 days	66SS+2 days
68	0%	Water Services	Thu 4/30/26	Wed 5/27/26	20 days	67SS+2 days
69	0%	Temporary Asphalt Patch	Fri 5/1/26	Thu 5/28/26	20 days	67SS+3 days
70	0%	Flushing/Testing/Disenfection	Tue 5/26/26	Mon 6/8/26	10 days	67
71	0%	Health Department Approval	Tue 6/9/26	Mon 6/29/26	15 days	70
72	0%	Water Service Transfers	Tue 6/30/26	Mon 7/20/26	15 days	71
73	**0%**	**Vacuum Sewer**	**Tue 7/21/26**	**Wed 12/2/26**	**97 days**	
74	0%	Erosion Control/BMPs	Tue 7/21/26	Wed 7/22/26	2 days	72
75	0%	MOT Inititial Setup	Thu 7/23/26	Fri 7/24/26	2 days	74
76	0%	Dewatering Systems	Mon 7/27/26	Wed 9/16/26	38 days	75
77	0%	AC Watermain Removals	Thu 9/17/26	Mon 11/9/26	38 days	76
78	0%	Vacuum Main/Pit Installation	Mon 9/21/26	Wed 11/11/26	38 days	77SS+2 days
79	0%	Temporary Asphalt Patch	Fri 9/25/26	Tue 11/17/26	38 days	77SS+6 days
80	0%	Flushing/Testing	Thu 11/12/26	Wed 12/2/26	15 days	78
81	0%	Substantial Completion	Wed 12/2/26	Wed 12/2/26	0 days	80
82	0%	Punchlist	Thu 12/3/26	Wed 12/23/26	15 days	81
83	0%	Permit Closeout	Thu 12/3/26	Wed 12/23/26	15 days	81
84	0%	Final Completion	Wed 12/23/26	Wed 12/23/26	0 days	82,83
