
File ID: W696-B1RU14
TASK filter: All Activities

Westra Construction Corp

WCC 696 - Hillsborough County - Ruskin Vac Sewer U14

Run Date: 08/19/26 15:52
Data Date: 08/01/26
Forecast Completion Date: 05/25/27

Activity ID	Activity Name	Page	Cal ID	Orig Dur	Rem Dur	Dur % Comp	Actual Start	Actual Finish	Start	Finish	Late Start	Late Finish	Total Float
WCC 696 - Hillsborough County - Ruskin Vac Sewer U14				510	204	60%	05/07/25		05/07/25 A	05/25/27	08/03/26	05/28/27	3
Milestones			7D	749	88	88.25%	05/07/25		05/07/25 A	05/25/27	08/03/26	05/28/27	3
M-010	GMP BOCC Approval		7D	0	0	100%	05/07/25		05/07/25 A		08/03/26		
M-020	Limited Notice to Proceed		7D	0	0	100%	05/08/25		05/08/25 A		08/03/26		
M-060	Notice to Proceed		7D	0	0	100%	06/09/25		06/09/25 A		08/06/26		
M-080	Substantial Completion		7D	0	0	0%				02/26/27*		02/27/27	1
M-090	Final Completion		7D	0	0	0%				05/25/27		05/28/27	3
Permits			7D	234	0	100%	05/08/25	09/17/25	05/08/25 A	09/17/25 A	08/06/26	08/21/26	
Procurement				350	45	87.14%	05/08/25		05/08/25 A	10/05/26	08/03/26	12/14/26	48
Prepare Submittals			5D	20	10	50%	05/08/25		05/08/25 A	08/14/26	08/03/26	12/02/26	74
Review & Approve			5D	327	25	92.35%	05/13/25		05/13/25 A	09/04/26	08/06/26	12/02/26	59
Release & Material Delivery				344	45	86.92%	06/05/25		06/05/25 A	10/05/26	08/06/26	12/14/26	48
Preliminary & On-Going			5D	498	203	59.24%	06/03/25		06/03/25 A	05/24/27	08/06/26	05/27/27	3
Construction				411	125	69.59%	06/10/25		06/10/25 A	02/02/27	08/06/26	03/03/27	21
Phase 1 - Vacuum Station			5D	339	93	72.57%	06/10/25		06/10/25 A	12/14/26	08/21/26	12/14/26	0
Phase 2			5D	411	125	69.59%	06/10/25		06/10/25 A	02/02/27	08/06/26	03/03/27	21
Pre-Construction			5D	54	0	100%	06/10/25	09/19/25	06/10/25 A	09/19/25 A	08/06/26	09/01/26	
Construct West Vac Main			5D	189	0	100%	09/22/25	06/15/26	09/22/25 A	06/15/26 A	08/06/26	08/06/26	
Westbound Shell Point Road (V1-14 to V1-9)			5D	138	0	100%	09/22/25	04/10/26	09/22/25 A	04/10/26 A	08/06/26	08/06/26	
Westbound Shell Point Road (V1-9 to V1-1)			5D	138	0	100%	12/05/25	06/15/26	12/05/25 A	06/15/26 A	08/06/26	08/06/26	
Forcemain East			5D	341	91	73.31%	06/10/25		06/10/25 A	12/10/26	08/17/26	12/29/26	10
Pre-Construction			5D	25	0	100%	06/10/25	06/23/25	06/10/25 A	06/23/25 A	08/17/26	08/17/26	
Construct FM West Shell Point Road			5D	100	0	100%	07/21/25	02/18/26	07/21/25 A	02/18/26 A	08/17/26	08/17/26	
Post Construction			5D	91	91	0%	01/16/26		01/16/26 A	12/10/26	08/17/26	12/29/26	10
Construct East Vac Station			5D	369	125	66.12%	07/24/25		07/24/25 A	02/02/27	09/01/26	03/03/27	21
Eastbound Shell Point Road (V2-1 to V2-9)			5D	247	5	97.98%	07/24/25		07/24/25 A	08/07/26	09/01/26	10/21/26	51
16th Street NW (V2-32 & V2-33)			5D	115	35	69.57%	03/02/26		03/02/26 A	09/28/26	09/09/26	10/27/26	21
12th Place NW (V2-31)			5D	117	47	59.83%	04/06/26		04/06/26 A	10/19/26	09/21/26	11/17/26	21
13th Street NW (V2-30 & V2-29)			5D	115	70	39.13%	04/24/26		04/24/26 A	11/09/26	09/28/26	12/10/26	21
West Shell Point Road (V2-28)			5D	103	15	85.44%	05/18/26		05/18/26 A	12/02/26	10/19/26	01/06/27	21
15th Street NW (V2-27 & V2-26)			5D	129	100	22.48%	05/29/26		05/29/26 A	12/23/26	10/19/26	01/27/27	21
Nethers Place (V2-25)			5D	102	0	100%	06/30/26	06/30/26	06/30/26 A	06/30/26 A	10/19/26	01/28/27	
22nd Street NW (V2-11 & V2-10)			5D	298	110	63.09%	08/27/25		08/27/25 A	01/12/27	10/07/26	02/11/27	21
21st Street NW (V2-13 & V2-12)			5D	306	125	59.15%	10/06/25		10/06/25 A	02/02/27	10/07/26	03/03/27	21
19th Street NW (V2-15 & V2-14)			5D	233	52	77.68%	11/21/25		11/21/25 A	10/14/26	09/01/26	11/12/26	21
18th Street NW & Morgan S. Lane (V2-19, V2-18 & V2-17)			5D	209	62	70.33%	01/07/26		01/07/26 A	10/28/26	09/23/26	12/01/26	21
Kofresi Court (V2-16)			5D	82	0	100%	02/11/26	02/20/26	02/11/26 A	02/20/26 A	10/07/26	12/01/26	
17th Street NW & W North Branch Road (V2-24, V2-21 & V2-20)			5D	161	77	52.17%	03/16/26		03/16/26 A	11/18/26	10/07/26	12/21/26	21
East North Branch Road (V2-22)			5D	131	87	33.59%	04/01/26		04/01/26 A	12/04/26	10/07/26	01/11/27	21
Middle Branch Road (V2-23)			5D	118	97	17.8%	03/27/26		03/27/26 A	12/18/26	10/19/26	01/22/27	21
Phase 3				154	110	28.57%	03/26/26		03/26/26 A	01/12/27	08/06/26	02/03/27	16
Pre-Construction			7D	0	0	0%	04/06/26	04/06/26	04/06/26 A	04/06/26 A	08/06/26	08/06/26	
Complete VM West of Vac Station			5D	154	110	28.57%	03/26/26		03/26/26 A	01/12/27	08/06/26	01/15/27	3
Janie Street (V1-20)			5D	85	42	50.59%	04/20/26		04/20/26 A	09/30/26	08/06/26	10/05/26	3
Steven Street (V1-19)			5D	73	57	21.92%	05/04/26		05/04/26 A	10/21/26	08/25/26	10/26/26	3
Carmelina Street (V1-18)			5D	111	67	39.64%	05/18/26		05/18/26 A	11/04/26	09/14/26	11/10/26	3
East of Marina (V1-17)			5D	126	15	88.1%	06/05/26		06/05/26 A	11/25/26	11/10/26	12/02/26	3
South Canal Street (V1-16)			5D	136	92	32.35%	04/06/26		04/06/26 A	12/11/26	10/16/26	12/16/26	3
North Canal Street (V1-15)			5D	102	102	0%	03/26/26		03/26/26 A	12/29/26	10/30/26	01/05/27	3
Post Construction			5D	110	110	0%			08/03/26	01/12/27	11/24/26	01/15/27	3
Post Construction			5D	97	97	0%			08/13/26	01/05/27	10/19/26	02/03/27	21
Close Out			5D	184	184	0%			08/31/26	05/25/27	11/04/26	05/28/27	3

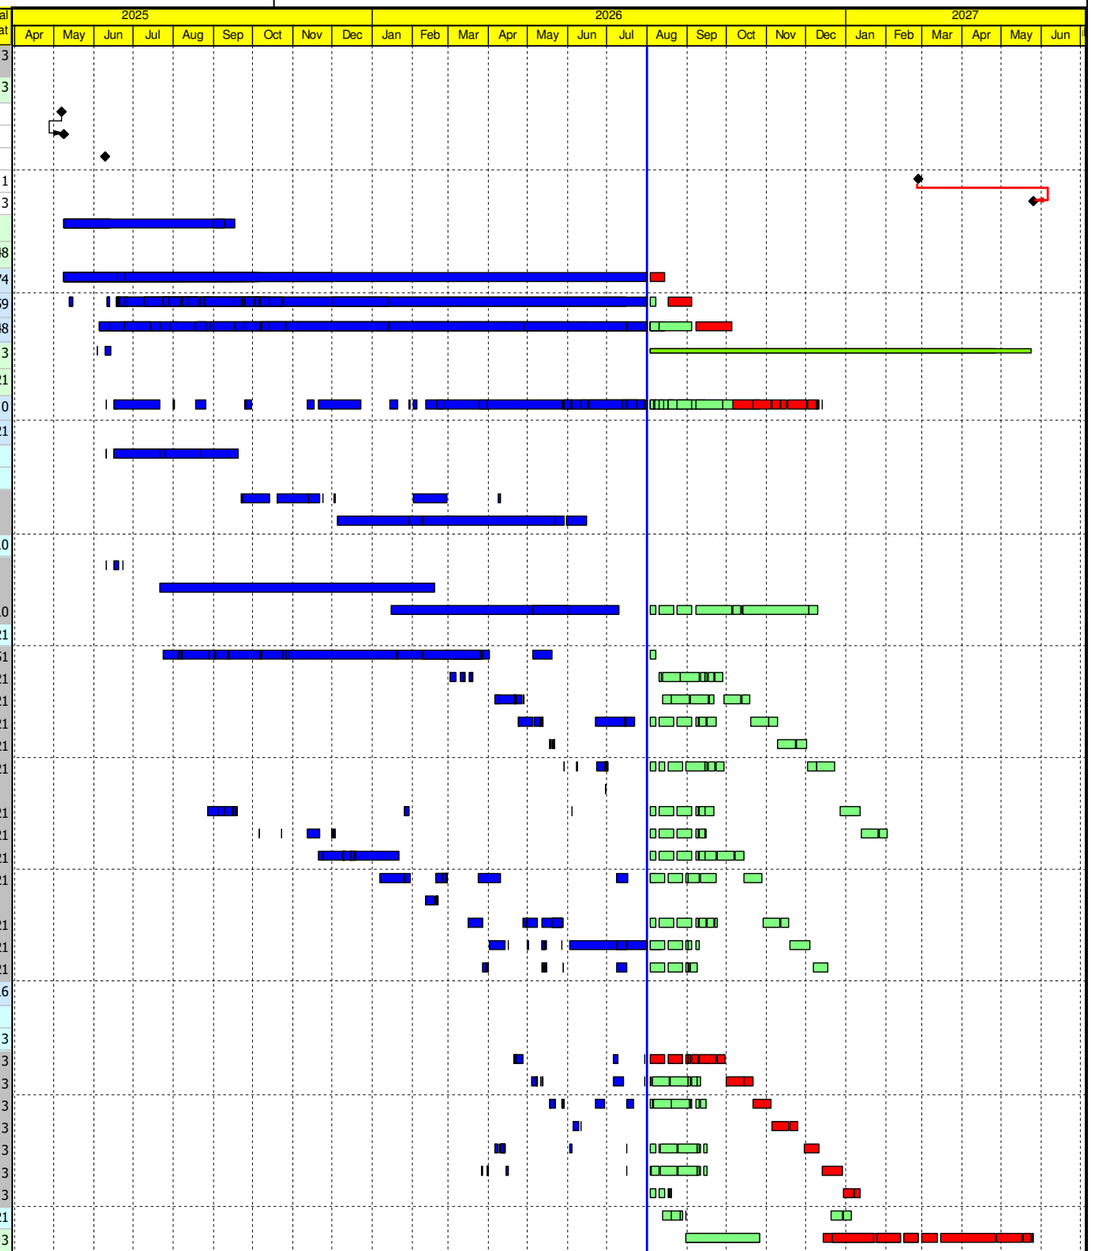

◆ Milestone ◆ Milestone | Critical Work | Actual LOE
Actual Work | Rem Work | Rem LOE

CPM prepared by FDOT DBE certified
Horses First, Inc. *before the cart!*
